

EXHIBIT 97



STATE OF NEW YORK

COUNTY OF NEW YORK

)
)
)
)

ss

CERTIFICATION

This is to certify that the attached translation is to the best of my knowledge and belief a true and accurate translation from Portuguese into English of the attached document with Bates number range EIG00155998 to EIG00156010.


A handwritten signature in black ink, appearing to read 'Edward J. Jacob'.

Edward J. Jacob
Divergent Language Solutions, LLC

State of New York

County of New York

Subscribed to and sworn before me this 11th day of May, 2021,
by Edward J. Jacob.

A handwritten signature in black ink, appearing to read 'Matthew C. Zelak'.
Notary Public



Executive Report

**APRIL
2015**

Rio de Janeiro, April 30, 2015


setebrasil

Confidential – Sete Brasil
IR Department

CONFIDENTIAL

This document is confidential and for the exclusive use of the shareholders and board members of Sete Brasil; it is prohibited to reproduce or disclose it to third parties, partially or fully, without the Company's prior, express authorization.



Executive Report – April 2015

Evolution of Assets (position on March 31, 2015)



Figure 1: DRU#1 Arpoador - Aracruz (Brazil) – April 2015

Rio de Janeiro, April 30, 2015 – As of late March 2015, the completed/consolidated physical progress for the twenty-nine rigs of the portfolio was 27.27%, compared to planned/consolidated physical progress of 34.80%. In comparison to February 2015, there was a worsening in the completed/planned ratio of 1.47 pp (physical progress is 7.54 pp below what was planned, compared to 6.07 pp the previous month).

The table below presents the main aspects of the projects' development over the month of March 2015.

Construction/Financial Progress	Physical Progress			Financial Progress	
	Status	Planned	Completed	Planned	Completed
Rigs					
Physical Progress/Consolidated Financial¹	●	34.80%	27.27%	49.12%	31.96%
1 st DRU (Arpoador @ Jurong)	●	97.82%	81.47%	95.99%	75.71%
2 nd DRU (Copacabana @ EAS)	●	86.33%	49.24%	97.49%	54.92%
3 rd DRU (Urca @ BrasFELS)	●	90.88%	87.72%	89.56%	71.04%
4 th DRU (Guarapari @ Jurong)	●	56.94%	61.79%	85.37%	62.65%
5 th DRU (Cassino @ ERG)	●	77.36%	52.24%	75.18%	53.12%
Construction/Auxiliary Projects at Shipyards					
EAS - Auxiliary Projects	●	100.00%	100.00%	-	-
Enseada - Construction ²	●	99.97%	81.50%	-	-
ERG 2 - Construction ³	●	100.00%	93.10%	-	-
EJA - Construction ²	●	99.73%	76.01%	-	-

(1) Order of rigs: start of Charter / Tiebreaker: delivery by the shipyard

(2) Cumulative progress completed by December 2014, as the shipyard did not indicate the progress from January 2015 to March 2015.

(3) Cumulative progress completed by November 2014, as the shipyard did not indicate the progress from December 2015 to March 2015.

The key highlights of the physical and financial evolution of Sete Brasil's assets in March 2015 are:

Jurong Aracruz Shipyard

Due to suspended services, EJA did not issue the Monthly Report in March 2015 (nor did it issue the February 2015 report) and consequently, physical progress was not reported for the period. The physical amounts completed refer to the cumulative amount as of January 2015.

DRU#1 Arpoador

- Began painting the helideck at EJA;
- Physical Progress Planned/Completed: 97.82%/81.47%.



DRU#7 Guarapari

- Completed assembly of blocks L6Q2, L6Q3, L6Q5, L6Q6, and painting of block L6Q4 of the EJA living quarters;
- Began assembly of the derrick on April 2 at EJA;
- Completed "engine cranks" (first rotation burning fuel), finishing the last one on April 10;
- Physical Progress Planned/Completed: 56.94%/61.79%.



Construction of Shipyard (EJA):

- Began installation of piping for facilities and launch of cables at workshop 1210.

BrasFELS Shipyard

The Shipyard did not provide notice that services were suspended, although the staff was reduced to on Saturdays and without any overtime system.

DRU#1 Urca

- On April 11, the load test on the seventh and last generator was performed (along with an inspection);
- Lifting and positioning of the *Mux Cable Reel Blue* on April 10;
- Prioritization of the Rig Line system, HPU, and their facilities to complete the commissioning of the rig drilling system;
- Physical Progress Planned/Completed: 90.88%/87.72%.



DRU#2 Frade

BrasFELS (Brazil)

- Topside: completed lifting of Megablock 1 (blocks 31/32S) on April 13.

Singapore

- Living Quarters: completed manufacture of piping and hook-ups for the cabins.
- Physical Progress Planned/Completed: 64.38%/59.56%.



DRU#3
Bracuhy

- Upper Columns (*Bintan*, Indonesia): completed the installation of equipment for Block 27 in April 2015.
- Physical Progress Planned/Completed: 37.74%/32.74%.



EAS Shipyard

Main Points:

- EAS issued a letter on January 26, 2015, indicating that work would be formally suspended as of February 3. It nonetheless noted that up to the end of February 2015, there were still a few services being performed at the shipyards in Brazil and abroad.
- Due to the services being suspended, there was no measurement in March 2015 and February 2015, and consequently no physical or financial progress during the period. The physical amounts completed refer to the cumulative amount as of January 2015.
- All sites had their projects effectively suspended in March 2015.
- The cumulative physical progress of DRU#2 was rectified with a 0.48% reduction, due to the lack of evidence from the shipyard proving the completed manufacture of four pieces of drilling equipment in the Drilling Package. Therefore, the consolidated physical progress of the shipyard went from 23.21% to 23.15%.

ERG2 Shipyard

The Shipyard did not provide notice that services would be suspended, but did drastically reduce its activities. Cosco extended the suspension of activities of the Cassino Project in China.

DRU#1
Cassino

ERG2

- Alignment of axis of mud agitators;
- Began assembly of mud mixer in block D25P.

China (Cosco)

- Installation of HVAC ducts;
- Living Quarters: finished paving floors and TH of firefighting system vessels;
- Physical Progress Planned/Completed: 77.35%/52.24%.



Enseada Shipyard

Main points:

- The shipyard informed the SPE that work would be suspended as of January 26, due to a failure to pay the amounts due. Despite this, work in Japan (construction of hulls) and China (construction of living blocks) are continuing to move forward for DRU#1 and ramping down for DRU#2. The activities in Maragojipe were effectively suspended on March 20 for DRU#2 and March 25 for DRU#1.
- The Shipyard suspended the weekly coordination, engineering, supply, and planning meetings, as well as the issuance of weekly reports and daily work reports.
- The cumulative amounts completed were calculated based on measurement #33 of March 2015. The amounts completed in February 2015 were reviewed after the completion of measurement #32 with regard to that month, which occurred after this report was issued.

Construction of Shipyard (ENSEADA):

- Demobilized the CEP workforce (Shipyard Construction Consortium) whose services will now be carried out by Enseada itself.
- Completed welding of the main beam of the Goliath Crane on April 10.

The chart below shows the consolidation of physical/financial progress and Local Content by shipyard:

Cumulative	Atlântico Sul Shipyard (EAS)		BrasFELS Shipyard (BrasFELS)		Jurong Aracruz Shipyard (EJA)		Rio Grande Shipyard (ERG 2)		Indústria Naval Shipyard (Enseada)	
	Planned	Completed	Planned	Completed	Planned	Completed	Planned	Completed	Planned	Completed
Physical Progress (%)	39.29%	23.15%	33.63%	33.01%	36.23%	34.03%	40.30%	24.82%	26.32%	19.66%
Financial Progress (%)	61.69%	36.29%	41.35%	29.50%	45.07%	35.14%	61.95%	35.17%	43.40%	25.03%
Construction/Auxiliary Projects (%)	100.00%	100.00%	Not applicable		99.73%	76.01%	100.00%	93.10%	99.97%	81.50%
Local Content ¹	DRU#1 = 60.19% Contractual: 55%		DRU#1 = 56.55% Contractual: 55%		DRU#1 = 60.21% Contractual: 55%		DRU#1 = 57.67% Contractual: 55%		DRU#1 = 57.12% Contractual: 55%	

¹Local Content Report:













- EAS with amounts of December 2014 (as we did not receive the January, February, and March 2015 Reports)
- EJA refers to January 2015 (as we did not receive the February and March 2015 Reports).

The payments scheduled for December 2014, January 2015, February 2015, and March 2015 were not made due to a lack of available cash by the SPEs, which resulted from the delay in disbursing the financing.

Monitoring of the Financing Plan

Short-term


The Company currently has five lines of short-term financing (Bridge Loan 3 was amortized) and one line of financing that was obtained from one of our shareholders, totaling approximately US\$3.7 billion.

Lender	Borrower	Rate	Maturity Date	Balance ¹	Comments
BRIDGE LOAN 1					
Itaú BBA and Banco do Brasil (US\$)	<ul style="list-style-type: none"> Copacabana Grumari Ipanema Leblon Leme 	Libor + 550 bps	February 2015	US\$734 million	Under Standstill – Awaiting restructuring
					
BRIDGE LOAN 2					
Bradesco, Banco do Brasil, and Santander (US\$)	<ul style="list-style-type: none"> Arpoador Cassino Urca Frade Guarapari Ondina Camburi 	Libor + 550 bps	February 2015	US\$1.717 million	Under Standstill – Awaiting restructuring
					
	<ul style="list-style-type: none"> Bracuhy Portogalo Pituba Boipeba Itaoca Curumim Salinas 	Libor + 400 bps	April 2015		Under Standstill – Awaiting restructuring
BRIDGE LOAN 3					
Sumitomo, Bradesco, Scotiabank, Citi, and Standard Chartered (US\$)	<ul style="list-style-type: none"> Sete International One GmbH 	N/A	N/A	US\$0 million	Loan amortized on January 14, 2015
					
					
					
BRIDGE LOAN 4					
Itaú BBA and Banco do Brasil (US\$)	<ul style="list-style-type: none"> Marambaia Interlagos Itapema Comandatuba Itaúnas Siri Sahy 	Libor + 390 bps	March 2015	US\$525 million	Under Standstill – Awaiting restructuring
					
BRIDGE LOAN 5					
Standard Chartered	<ul style="list-style-type: none"> Joatinga 	Libor + 200 bps	February 2015	US\$251 million	Execution process commenced in March 2015
					
BRIDGE LOAN 6					
Caixa Econômica Federal	<ul style="list-style-type: none"> Sete Investimentos I S.A. 	9.2% + Exchange rate variation	April 2015	US\$413 million	Under Standstill – Awaiting restructuring
					
EXCHANGEABLE					
Luce Venture Capital	<ul style="list-style-type: none"> Sete International One GmbH 	Libor + 4.75% per annum	December 2015	US\$46.5 million	N/A

(1) Position on April 30, 2015 with current conditions for matured loans.

Long-Term

The chart below shows the status of financing for each batch:

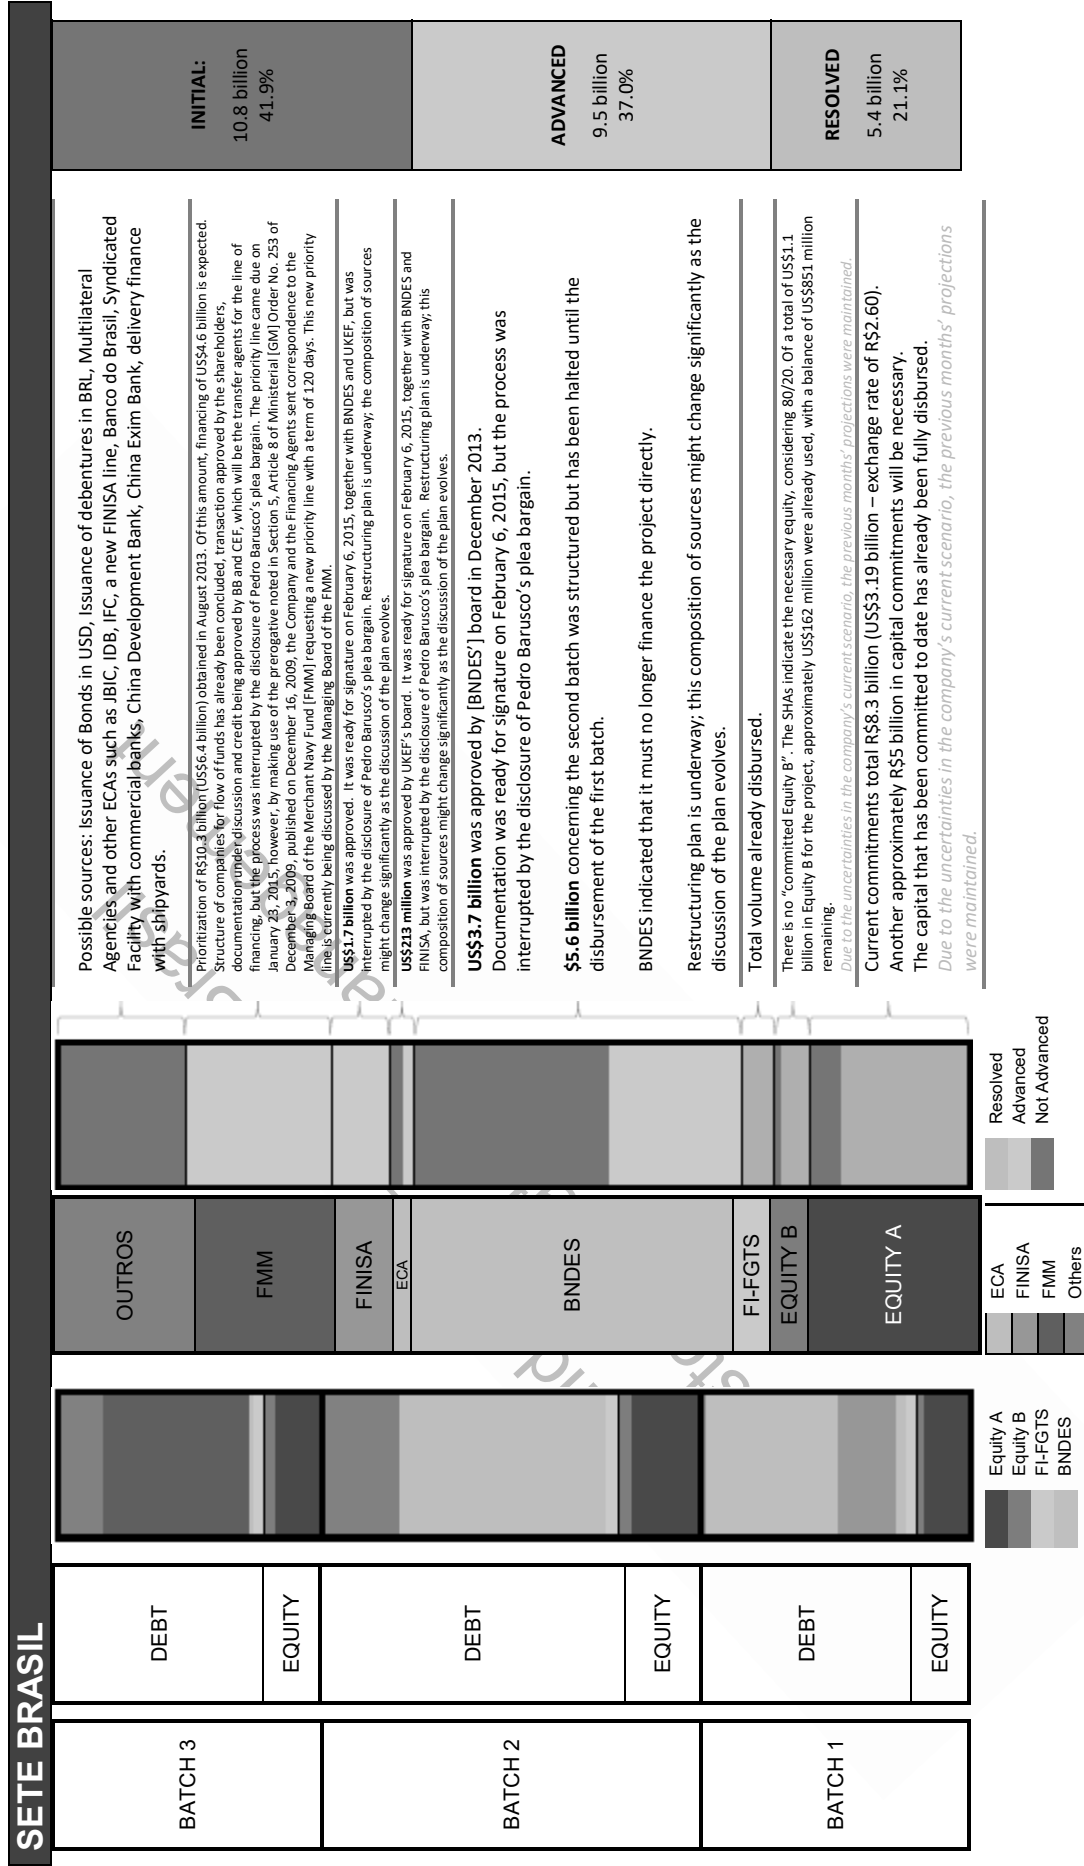

Financial Planning

As indicated by the Company's CFO at a Board of Director's Meeting on February 25, 2015, where certain shareholders were present, given the uncertainties of Sete Brasil's current situation, the Finance Division will not provide a cash flow projection. Therefore, as for the past two months, the information related to Financial Planning only takes into account what has already been fulfilled.

Chart of Uses and Sources

Obtained by March 2015

In millions of dollars

Uses			Sources		
	US\$	%		US\$	%
EPC Contract	7,215	92%	Bridge Loan	3,041	39%
Readjustment of EPC	484	6%	Loan	2,955	38%
Exchange Rate Variation of EPC	-718	-9%	BNDES	0	0%
Pre-Operating Costs	0	0%	ECAs	0	0%
Contingencies	0	0%	FMM	0	0%
CMA - Petrobras	87	1%	Other (Finisa/Bonds/Others)	0	0%
CMA - Operators	116	1%	Total Debt	5,996	77%
CMA - Sete Brasil	0	0%			
Certification	0	0%			
Insurance	129	2%	Equity Class A	822	11%
FGCN	34	0%	Equity Class B	162	2%
Financial Costs	218	3%	FI-FGTS	743	10%
			Total Capital	1,727	22%
G&A and Other	220	3%	Other	81	1%
Cash	18	0%			
TOTAL	7,804	100%	TOTAL	7,804	100%

*Amounts take cash activity into consideration (these amounts do not include accounting information such as interest capitalizations)

The Chart on Uses and Sources consolidates all expenses of the SPEs incurred by March 2015, including CAPEX and administrative expenses, providing the details for the sources used to bear the costs of these investments.

Note that approximately 39% of the investments were paid for with funds from financing taken out directly within the SPEs (Bridge Loans 1, 2, and 4), 10% were paid using funds from FI-FGTS, and 38% were paid using loans from shareholders' funds. The remaining 13% refer to equity classes A and B.

Although each SPE has distinct leverage indices, as demonstrated in the item "Control of SPE debts and contributions," the consolidation of the SPEs strives for a target capital structure of 75% debt and 25% equity. Each SPE's individual planning considers equalizing all of them at the level required by the long-term lenders at the time of their first disbursement.

CONTROL OF SPE DEBTS AND CONTRIBUTIONS

March 2015

Amounts in Dollars

COMPANY	SHIPYARD	CLASS B	TOTAL					% Stake		Debt - Equity Ratio		
			CLASS A	CLASS B	INTERCO - FI FGTS ¹	INTERCOMPANY ²	BRIDGE LOAN ³	CLASS A	CLASS B	Equity	Debt	D/E
ARPOADOR	JURONG	PNBV	81,347,617	14,350,538	29,495,217	207,914,619	287,076,532	85%	15%	125,193,372	494,991,151	20%
COPACABANA	EAS	PNBV	67,921,489	11,981,221	26,200,010	172,450,065	146,991,153	85%	15%	106,102,720	319,441,218	25%
GRUMARI	EAS	PNBV	54,593,352	9,629,197	27,052,691	125,600,890	148,311,667	85%	15%	91,138,240	273,912,557	25%
IPANEMA	EAS	PNBV	35,681,459	6,291,804	27,052,986	68,873,258	136,860,170	85%	15%	69,026,249	205,733,428	25%
LEBLON	EAS	PNBV	29,166,841	5,142,165	21,967,095	31,218,432	136,860,170	85%	15%	56,276,101	168,078,602	25%
LEWE	EAS	PNBV	27,247,385	4,803,438	22,069,328	24,785,492	136,860,170	85%	15%	54,120,151	161,645,662	25%
MARABAIÁ	EAS	PNBV	26,894,796	4,741,216	22,450,150	8,537,499	152,165,000	85%	15%	54,086,768	160,702,499	25%
URCA	BRASFELS	ANGRA PART. (QGOG)	73,550,291	12,944,158	38,116,700	174,592,552	313,783,883	85%	15%	124,411,149	488,376,435	20%
GUARAPARI	JURONG	ODF-ELL GALVÃO	57,526,787	14,389,181	42,068,051	250,799,261	182,484,139	80%	20%	114,014,019	433,283,400	21%
BRACHUY	BRASFELS	ANGRA PART. (QGOG)	19,726,626	3,481,158	34,694,149	194,652,180	30,885,066	85%	15%	57,901,933	225,537,246	20%
PORTOGALO	BRASFELS	DOMAIN (PETROSERV)	5,987,185	1,056,551	15,041,185	54,998,727	30,527,619	85%	15%	22,087,921	85,526,346	21%
MANGARATIBA	BRASFELS	ANGRA PART. (QGOG)	6,055,185	1,068,551	12,572,018	77,050,433	-	85%	15%	19,695,754	77,143,186	20%
BOTINAS	BRASFELS	NEPTUNE (OOG)	60,935,255	10,753,268	36,260,142	227,323,169	201,894,935	85%	15%	19,802,475	77,050,433	20%
ONDINA	PARAGUACU	NEPTUNE (OOG)	20,317,661	3,585,458	31,751,018	179,648,803	44,544,867	85%	15%	107,948,665	429,218,104	20%
PUTIBA	PARAGUACU	NEPTUNE (OOG)	13,018,385	2,297,351	20,800,000	101,423,466	44,054,768	85%	15%	55,654,137	224,193,670	20%
BOPEBA	PARAGUACU	NEPTUNE (OOG)	6,422,385	1,133,351	22,806,160	23,050,001	37,000,000	85%	15%	36,115,736	145,478,234	20%
INTERLAGOS	PARAGUACU	SEAWORTHY (ETESCO/OAS)	8,021,812	2,673,924	23,156,160	1	34,000,000	75%	25%	30,361,896	60,050,001	34%
ITAPEWA	PARAGUACU	SEAWORTHY (ETESCO/OAS)	8,021,812	2,673,924	23,156,160	1	34,000,000	75%	25%	33,851,896	34,000,001	50%
COMANDATUBA	PARAGUACU	SEAWORTHY (ETESCO/OAS)	8,021,812	2,673,924	23,156,160	1	34,000,000	75%	25%	33,851,896	34,000,001	50%
FRADE	BRASFELS	DOMAIN (PETROSERV)	35,790,106	6,260,820	40,285,554	288,548,515	40,693,598	85%	15%	82,336,480	329,242,113	20%
CAMBURI	JURONG	SEABRAS (SEADRILL)	14,524,036	6,224,558	36,623,130	140,093,441	89,027,141	70%	30%	57,371,724	229,120,582	20%
ITAOCÁ	JURONG	ODF-ELL GALVÃO	9,861,003	2,465,235	27,559,600	89,620,948	70,905,276	80%	20%	39,885,838	160,526,224	20%
ITAUNAS	JURONG	SEABRAS (SEADRILL)	7,023,635	3,010,101	27,454,747	39,700,000	95,835,000	70%	30%	37,488,483	135,535,000	22%
SIRI	JURONG	ODF-ELL GALVÃO	11,012,282	2,753,054	37,728,000	21,800,001	76,000,000	80%	20%	51,493,336	97,800,001	34%
SAHY	JURONG	SEABRAS (SEADRILL)	8,685,435	3,722,301	38,872,160	20,200,000	71,000,000	70%	30%	51,279,896	91,200,000	36%
CASSINO	ECOVIX	SEAWORTHY (ETESCO/OAS)	45,208,829	14,743,212	31,292,953	204,521,733	157,945,554	75%	25%	91,244,994	362,467,287	20%
CURUMIM	ECOVIX	SEAWORTHY (ETESCO/OAS)	17,824,302	5,941,434	33,612,920	114,622,469	99,519,864	75%	25%	57,378,656	214,142,333	21%
SALINAS	ECOVIX	SEAWORTHY (ETESCO/OAS)	17,320,302	5,773,434	21,443,200	75,471,334	85,662,150	75%	25%	44,536,936	161,133,484	22%
JOATINGA	EAS	ASD	46,045,637	-	-	52,900,000	250,000,000	100%	0%	46,045,637	302,900,000	13%
TOTAL			821,617,075	164,959,154	784,126,828	3,047,540,473	3,134,888,721			1,770,703,057	6,182,429,194	22%

* Book values (include capitalization of interest, where applicable, for Intercompanies and Bridges).

1	INTERCO - FI FGTS	Long-term subordinate loans using funds from FI-FGTS Debentures. In the SPEs these are loans with a fifteen-year amortization term, a total grace period of nine months after the start of the operation, with 12% interest per annum. In order to calculate leverage, these funds are considered to be equity.
2	INTERCOMPANY	Short-term (bridge) loans with funds from Bridge Loan 3, taken at Sete International, and/or shareholder funds. They will be repaid when new bridge financing is obtained (e.g., Bridge Loan 4) taken directly within the SPE or when the senior debt is disbursed. In cases of SPEs that have taken out a bridge loan, this is a Subordinate Instrument.
3	BRIDGE	Short-term loans taken out directly by the SPE (Bridge Loans 1, 2, and 4). They will be repaid at the time of the first disbursement of the senior debt.

General Highlights

GOVERNANCE

Board of Directors

Board of Directors Meeting of April 15, 2015

Matters for deliberation:

- Deliberated on revising criteria for the benefits of directors' long-term compensation.

Informational Matters:

- Overview of the Company's Business;
- Monitoring of the Company's Financing Plan;
- Monitoring of evolution of assets;
- Internal Audit Report.

Audit Committee

Meeting April 9, 2015

- Internal Audit Report.

Fiscal Council

Meeting of the Fiscal Council April 14, 2015

- Budget Follow-up (budgeted x actual) up to February 2015.

General Meeting

General Meeting of Shareholders April 30, 2015 11:00 a.m.

- Meeting of shareholders pending formal closure (until the date of disclosure of this Report).


Special Meeting of Shareholders April 30, 2015 12:00 p.m.

- Meeting temporarily open (until the date of disclosure of this Report);
- Agenda: deliberate on authorizing the Company to start pre-operational preparations for the drilling rigs of the Rigs Project.

REGARDING SETE BRASIL

Formed in December 2010, Sete Brasil is a privately-held corporation specialized in asset portfolio management with investments geared towards the oil and gas sector of the offshore area in Brazil, particularly those related to the Brazilian Pre-Salt Basin. Sete Brasil's project portfolio contains twenty-eight charter contracts and twenty-nine EPC contracts; its portfolio of operational assets is divided into twenty-three drillship-type units and six semisubmersible-type units. The Company was created with Petrobras and the private equity fund FIP Sondas (comprised of institutional investors, banks, and investment funds), as its direct shareholders.


Corporate Structure

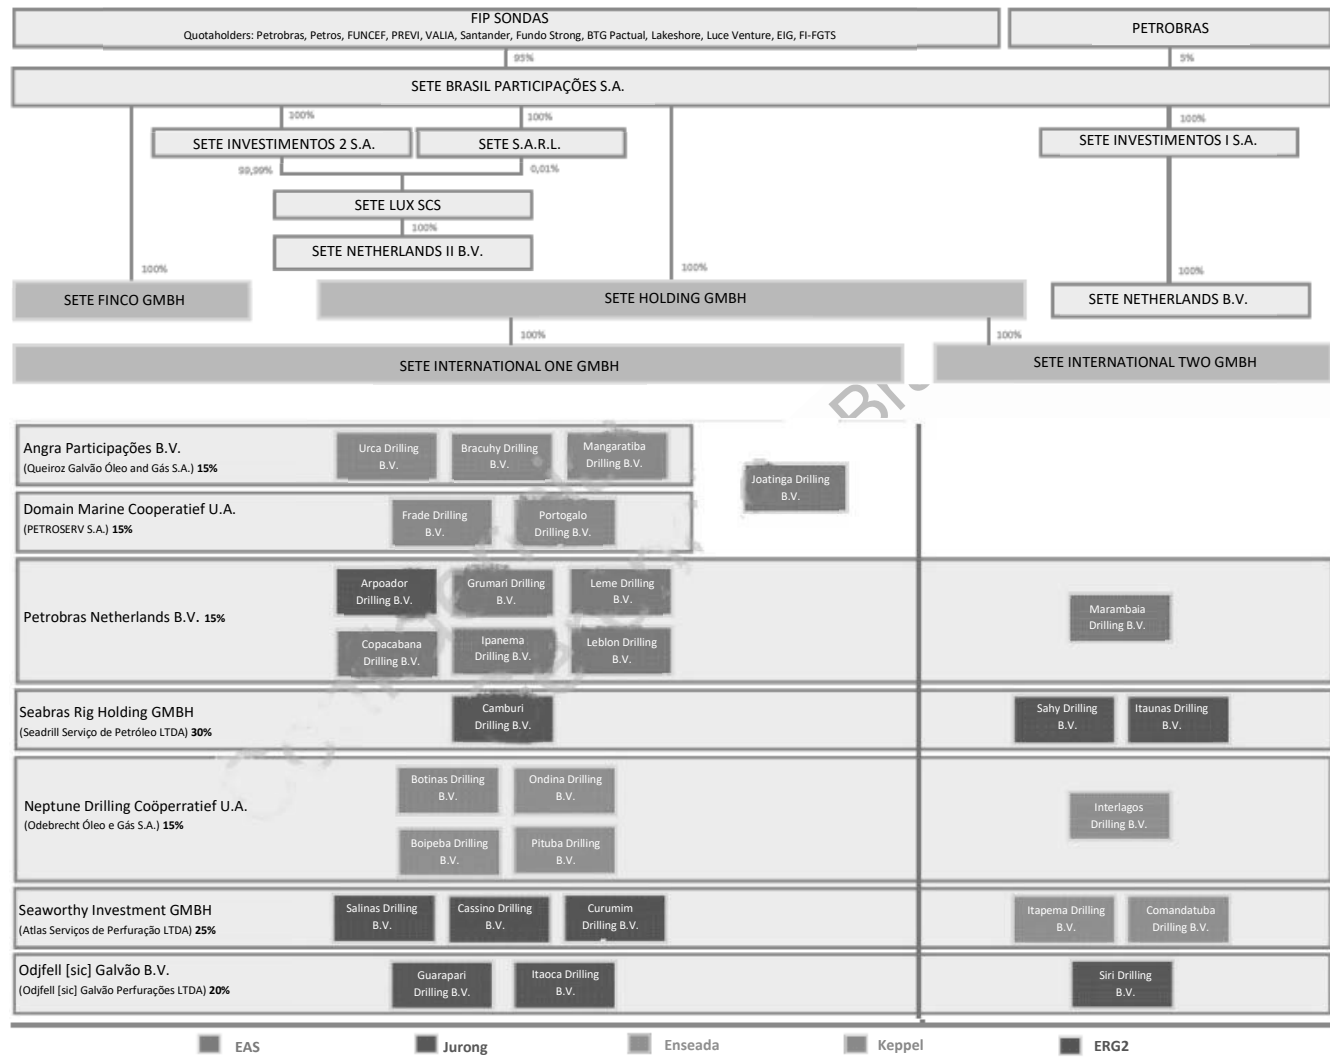

Investor Relations Department

ri@setebr.com
www.setebr.com
<http://ri.setebr.com/>
+ 55 21 2528-0080



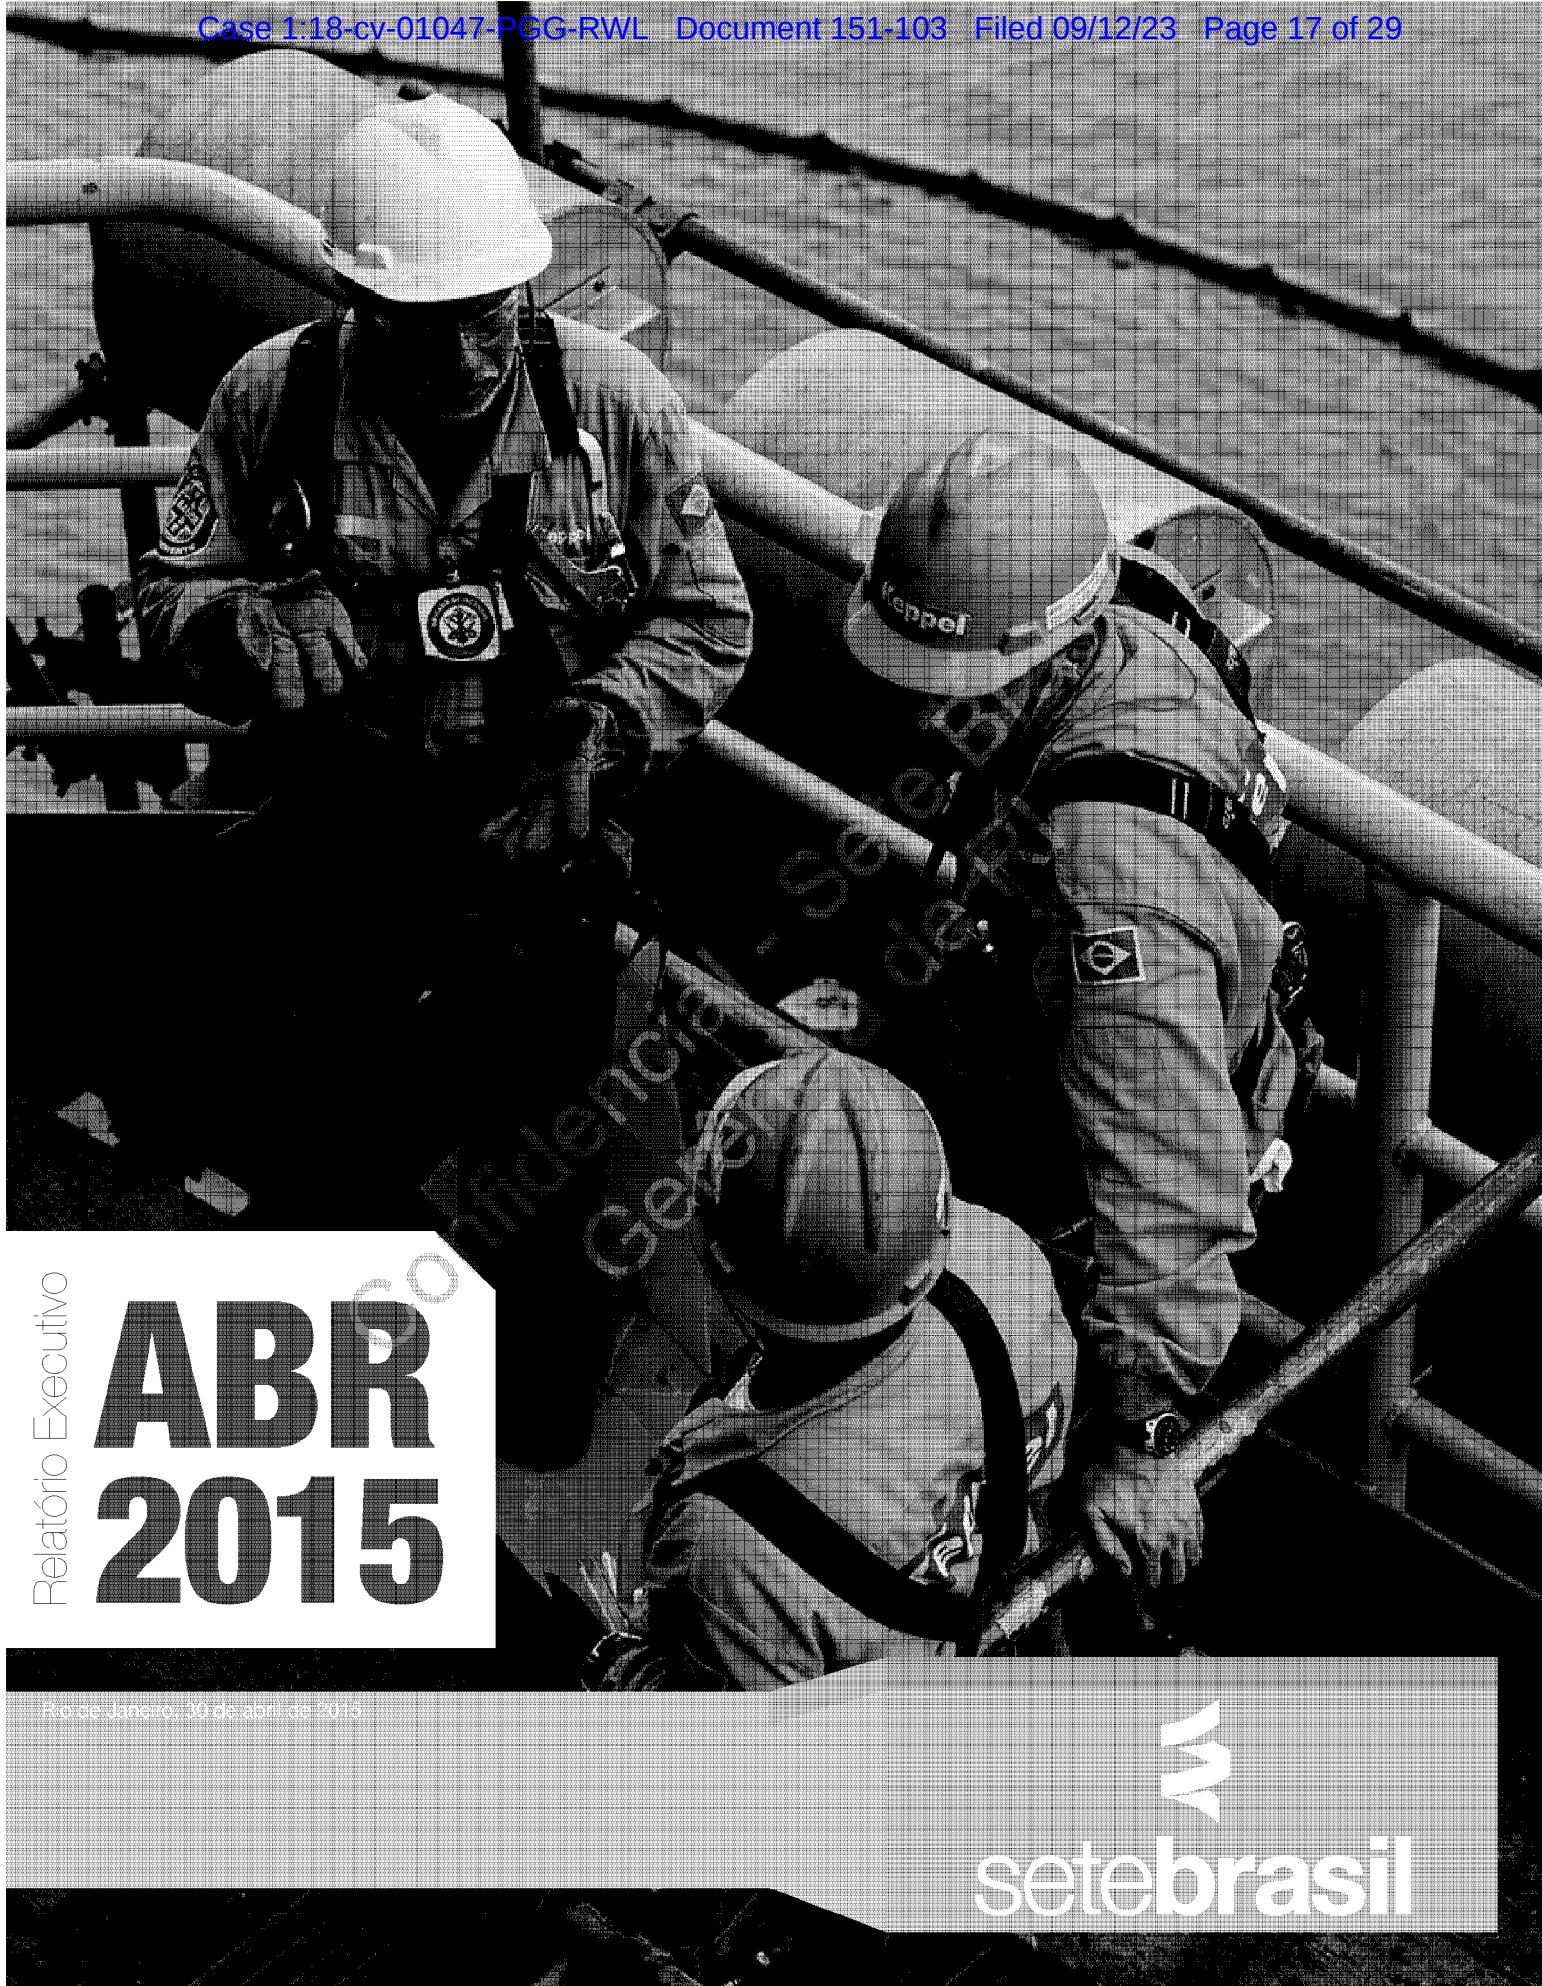

Relatório Executivo

ABR 2015

Rio de Janeiro, 30 de abril de 2015




setebrasil

Confidencial - Sete Brasil
Gerência de RI

CONFIDENCIAL

Este documento é confidencial e de uso exclusivo dos acionistas e conselheiros da Sete Brasil, sendo vedada sua reprodução e divulgação a terceiros, no todo ou em parte, sem a prévia autorização expressa da Companhia.



Relatório Executivo - Abril/2015

Evolução da Constituição dos Ativos (posição em 31.03.2015)



Figura 1: DRU#1 Arpoador - Aracruz (Brasil) - abril/2015

Rio de Janeiro, 30 de abril de 2015 - No final do mês de março/15, o avanço físico realizado/consolidado para as 29 sondas do portfólio foi de 27,27%, contra um avanço físico planejado/consolidado de 34,80%. Em comparação ao mês de fevereiro/15, houve uma piora na relação realizado/planejado em 1,47pp (avanço físico está 7,54pp abaixo do planejado, contra 6,07pp no mês anterior).

A tabela a seguir apresenta os principais aspectos da evolução das obras durante o mês de março/15.

Avanço Construção/Financeiro	Avanço Físico			Avanço Financeiro	
	Status	Planejado	Realizado	Planejado	Realizado
Sondas					
Avanço Físico/Financeiro Consolidado¹	●	34,80%	27,27%	49,12%	31,96%
1ª DRU (Arpoador @ Jurong)	●	97,82%	81,47%	95,99%	75,71%
2ª DRU (Copacabana @ EAS)	●	86,33%	49,24%	97,49%	54,92%
3ª DRU (Urca @ BrasFELS)	●	90,88%	87,72%	89,56%	71,04%
4ª DRU (Guarapari @ Jurong)	●	56,94%	61,79%	85,37%	62,65%
5ª DRU (Cassino @ ERG)	●	77,36%	52,24%	75,18%	53,12%
Construção / Obras Auxiliares Estaleiros					
EAS - Obras Auxiliares	●	100,00%	100,00%	-	-
Enseada - Construção ²	●	99,97%	81,50%	-	-
ERG 2 - Construção ³	●	100,00%	93,10%	-	-
EJA - Construção ²	●	99,73%	76,01%	-	-

(1) Ordem das sondas: início do Afretamento / Desempate: entrega pelo estaleiro

(2) Avanço Realizado acumulado até Dez/14, pois o estaleiro não informou os avanços de Jan/15 a Mar/15.

(3) Avanço Realizado acumulado até Nov/14, pois o estaleiro não informou os avanços de Dez/15 a Mar/15.


Os principais destaques da evolução física e financeira da constituição dos ativos da Sete Brasil no mês de março/15 são:

Estaleiro Jurong Aracruz

Em virtude da suspensão dos serviços, o EJA não emitiu o Relatório Mensal de março/15 (assim como o de fevereiro/15), e, conseqüentemente, não foram reportados avanços físicos para o período. Os valores físicos realizados referem-se ao acumulado até janeiro/15.


DRU#1 Arpoador

- Iniciada a pintura do *Helideck* no EJA;
- Avanço Físico Planejado/Realizado: 97,82% / 81,47%.

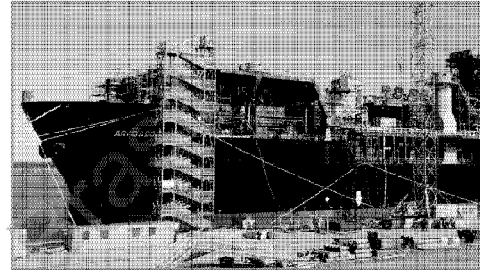

DRU#7 Guarapari

- Finalizada a montagem dos blocos L6Q2, L6Q3, L6Q5, L6Q6 e pintura do bloco L6Q4 do *Living Quarter* no EJA;
- Iniciada a montagem do *Derrick* em 02/abril no EJA;
- Realização do "Crank dos Motores" (primeiro giro com queima de combustível), sendo o último em 10/abril;
- Avanço Físico Planejado/Realizado: 56,94% / 61,79%.

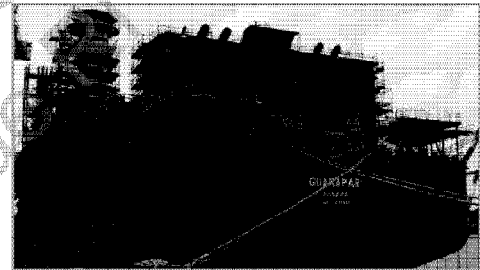

Construção do Estaleiro (EJA):


- Iniciada a instalação de tubulação para facilidades e lançamento de cabos na oficina 1210.

Estaleiro BrasFELS

O Estaleiro não notificou a suspensão dos serviços, porém o efetivo foi reduzido aos sábados e sem regime de horas extras.

DRU#1 Urca

- Em 11/abril foi realizado (e acompanhado pela fiscalização) o *load test* do 7º e último gerador;
- Içamento e posicionamento do *Mux Cable Reel Blue* em 10/abril;
- Priorização do sistema de *Rig Line*, HPU e suas facilidades para o desenvolvimento do comissionamento do sistema de *drilling* da sonda;
- Avanço Físico Planejado/Realizado: 90,88% / 87,72%.

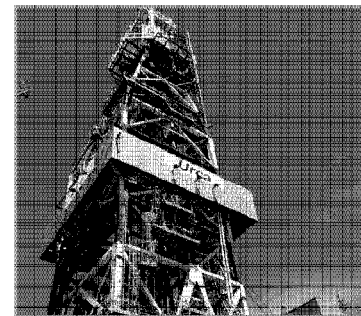

DRU#2 Frade

BrasFELS (Brasil)

- *Topside*: realizado *lifting* do Megabloco 1 (blocos 31/32S) em 13/abril.


Cingapura

- *Living Quarter*: concluída a fabricação de tubulação e *hook-ups* para as cabines.
- Avanço Físico Planejado/Realizado: 64,38% / 59,56%.



DRU#3 Brachy

- *Upper Columns (Bintan, Indonésia)*: concluída a instalação de equipamentos do bloco 27 em abril/15.
- Avanço Físico Planejado/Realizado: 37,74% / 32,74%.

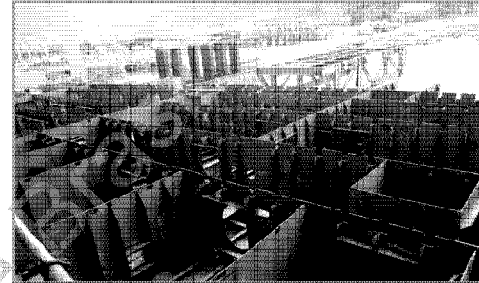**Estaleiro EAS**

Principais pontos:

- O EAS emitiu uma carta, em 26 de janeiro de 2015, informando sobre a suspensão formal dos trabalhos a partir do dia 03/fevereiro. Apesar disso, observou-se que até o final do mês de fevereiro/15 ainda houve execução de alguns poucos serviços nos estaleiros no Brasil e no exterior.
- Em virtude da suspensão dos serviços, não houve medição em março/15 e fevereiro/15, e, conseqüentemente, não houve avanço físico e financeiro no período. Os valores físicos realizados referem-se ao acumulado até janeiro/15.
- Todos os sites tiveram suas obras paralisadas efetivamente em março/15.
- O progresso físico acumulado da DRU#2 foi retificado, com uma redução de 0,48%, devido à falta de evidências apresentadas pelo estaleiro que comprovem o fim da fabricação de quatro equipamentos do *Drilling Package*. Com isso, o avanço físico consolidado do estaleiro passa de 23,21% para 23,15%.

Estaleiro ERG2

O Estaleiro não notificou a paralisação dos serviços, porém reduziu drasticamente as atividades. A Cosco reforçou a suspensão das atividades do Projeto Cassino na China.


DRU#1
Cassino

ERG2

- Alinhamento de eixo dos agitadores de lama;
- Início da montagem do *Mud Mixer* no bloco D25P.

China (Cosco)

- Instalação de dutos de HVAC;
- Módulo de Acomodações: conclusão da pavimentação dos pisos e TH de vasos do sistema de combate a incêndios;
- Avanço Físico Planejado/Realizado: 77,35% / 52,24%.

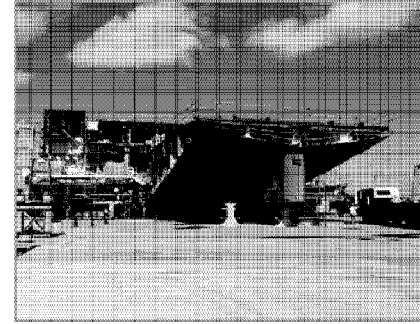

Estaleiro Enseada

Principais pontos:

- O Estaleiro notificou a SPE sobre a suspensão dos trabalhos a partir de 26/janeiro, devido ao não pagamento dos valores devidos. Apesar disso, os trabalhos no Japão (construção dos cascos) e China (construção dos blocos de acomodações) continuam em andamento para a DRU#1 e desacelerando para a DRU#2. As atividades em Maragogipe foram efetivamente suspensas em 20/março para DRU#2 e 25/março para DRU#1.
- O Estaleiro suspendeu as reuniões semanais de coordenação, engenharia, suprimento e planejamento, bem como a emissão dos relatórios semanais e RDO.
- Os valores realizados acumulados foram calculados com base na medição #33 de março/15. Os valores realizados de fevereiro/15 foram revisados após a conclusão da medição #32 referente à aquele mês, que ocorreu posteriormente à emissão deste relatório.

Construção do Estaleiro (ENSEADA):

- Desmobilizada a mão de obra do CEP (Consórcio construtor do Estaleiro) cujos serviços passam a ser realizados pelo próprio Enseada.
- Concluída a soldagem da Viga Principal do *Goliath Crane* em 10/abril.

A seguir, a tabela com o consolidado do avanço físico/financeiro e Conteúdo Local por estaleiro:

Acumulado	Estaleiro Adherson Sul (EAS)		Estaleiro BrasFEL3 (BrasFEL3)		Estaleiro Jurong Aracruz (EJA)		Estaleiro Rio Grande (ERG 2)		Enseada Industrial Naval (Enseada)	
	Planejado	Realizado	Planejado	Realizado	Planejado	Realizado	Planejado	Realizado	Planejado	Realizado
Avanço Físico (%)	39,29%	23,15%	33,63%	33,01%	36,23%	34,03%	40,30%	24,82%	26,32%	19,66%
Avanço Financeiro (%)	61,69%	36,29%	41,35%	29,50%	45,07%	35,14%	61,95%	35,17%	43,40%	25,03%
Construção/ Obras Auxiliares (%)	100,00%	100,00%	Não aplicável		99,73%	76,01%	100,00%	93,10%	99,97%	81,50%
Conteúdo Local¹	DRU#1 = 60,19% Contratual: 55%		DRU#1 = 56,55% Contratual: 55%		DRU#1 = 60,21% Contratual: 55%		DRU#1 = 57,67% Contratual: 55%		DRU#1 = 57,12% Contratual: 55%	

¹Relatório de Conteúdo Local:

- EAS com valores de Dez/14 (pois não recebemos os Relatórios de Jan, Fev e Mar/15)

- EJA referente à Jan/15 (pois não recebemos os Relatórios de Fev e Mar/15).

Os pagamentos previstos para dezembro/14, janeiro/15, fevereiro/15 e março/15 não foram realizados em função da indisponibilidade de caixa pelas SPE, devido ao atraso no desembolso do financiamento.

Acompanhamento do Plano de Financiamento

Curto Prazo

Atualmente, a Companhia possui cinco linhas de financiamento de curto prazo contratadas (*Bridge 3* foi amortizado) e uma linha de financiamento obtida com um de nossos acionistas, totalizando cerca de US\$ 3,7 bi contratados.


Credor	Tomador	Taxa	Vencimento	Saldo ⁽¹⁾	Comentários
BRIDGE 1					
Itaú BBA e Banco do Brasil (US\$)	<ul style="list-style-type: none"> Copacabana Grumari Ipanema Leblon Leme 	Libor + 550 bps	Fevereiro-15	US\$ 734 mm	Em <i>Standstill</i> -Aguardando reestruturação-
BRIDGE 2					
Bradesco, Banco do Brasil e Santander (US\$)	<ul style="list-style-type: none"> Arpoador Cassino Urca Frade Guarapari Ondina Camburi 	Libor + 550 bps	Fevereiro-15	US\$ 1.717 mm	Em <i>Standstill</i> -Aguardando reestruturação-
	<ul style="list-style-type: none"> Braculy Portogalo Pituba Boipeba Itaoca Curumim Salinas 	Libor + 400 bps	Abril-15		Em <i>Standstill</i> -Aguardando reestruturação-
BRIDGE 3					
Sumitomo, Bradesco, Scotiabank, Citi e Standard Chartered (US\$)	<ul style="list-style-type: none"> Sete International One GmbH 	N/A	N/A	US\$ 0 mm	Empréstimo amortizado em 14-Janeiro-2015
BRIDGE 4					
Itaú BBA e Banco do Brasil (US\$)	<ul style="list-style-type: none"> Marambala Interlagos Itapema Comandatuba Itaúnas Siri Sahy 	Libor + 390 bps	Março-15	US\$ 525 mm	Em <i>Standstill</i> -Aguardando reestruturação-
BRIDGE 5					
Standard Chartered	<ul style="list-style-type: none"> Joatinga 	Libor + 200 bps	Fevereiro-15	US\$ 251 mm	Processo de execução iniciado em Março-2015
BRIDGE 6					
Caixa Econômica Federal	<ul style="list-style-type: none"> Sete Investimentos I S.A. 	9,2%+ Variação Cambial	Abril-15	US\$ 413 mm	Em <i>Standstill</i> -Aguardando reestruturação-
EXCHANGEABLE					
Luce Venture Capital	<ul style="list-style-type: none"> Sete International One GmbH 	Libor + 4,75%aa	Dezembro-15	US\$ 46,5 mm	N/A

(1) Posição de 30/04/15 com condições vigentes para os empréstimos vencidos.

Longo Prazo

Abaixo, o gráfico com status por *batch* de cada financiamento:

SETE BRASIL

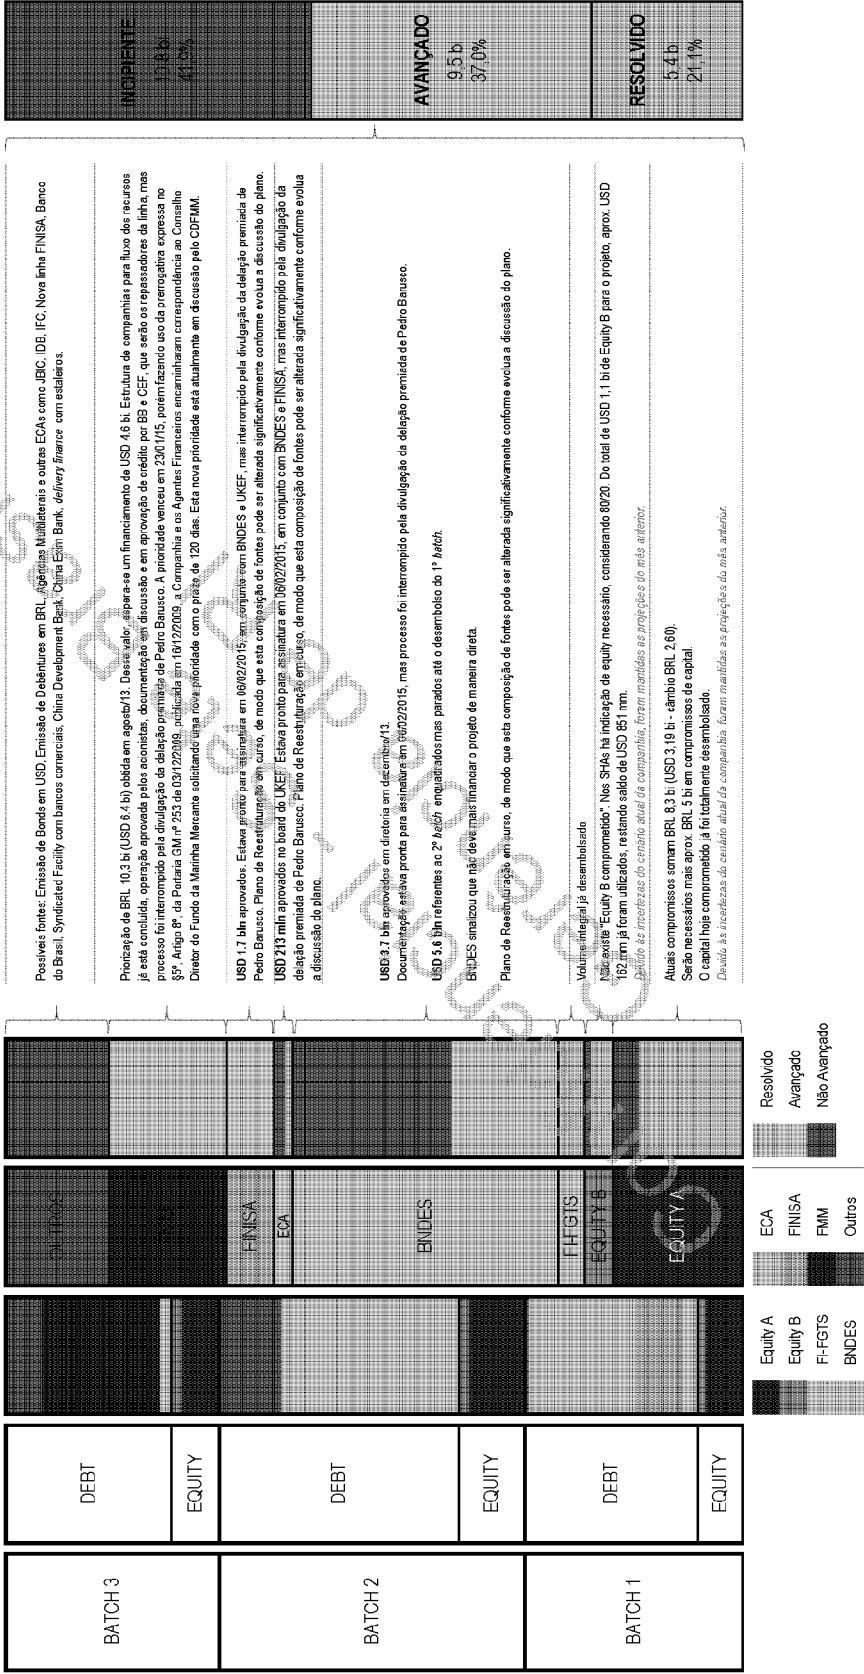

Planejamento Financeiro

Conforme informado pelo Diretor Financeiro da Companhia, em Reunião do Conselho de Administração de 25 de fevereiro de 2015, que contou com a presença de alguns acionistas, diante das incertezas do atual cenário da Sete Brasil, a Diretoria Financeira não fornecerá projeção de Fluxo de Caixa. Logo, conforme ocorrido nos dois últimos meses, as informações relacionadas ao Planejamento Financeiro só contemplam o realizado.

Quadro de Usos e Fontes

Realizado até Março-15

Em milhões de Dólares

Usos			Fontes		
	US\$	%		US\$	%
Contrato de EPC	7.215	92%	Bridge	3.041	39%
Reajuste do EPC	484	6%	Mútuo	2.955	38%
Variação Cambial do EPC	-718	-9%	BNDES	0	0%
Custos Pré-Operacionais	0	0%	ECAs	0	0%
Contingências	0	0%	FMM	0	0%
CMA - Petrobras	87	1%	Outros (Finisa/Bonds/Outros)	0	0%
CMA - Operadores	116	1%	Dívida Total	5.996	77%
CMA - Sete Brasil	0	0%			
Certificação	0	0%	Equity Class A	822	11%
Seguros	129	2%	Equity Class B	162	2%
FGCN	34	0%	FLFGTS	743	10%
Custos Financeiros	218	3%	Capital Total	1.727	22%
G&A e Outros	220	3%	Outros	81	1%
Caixa	18	0%			
TOTAL	7.804	100%	TOTAL	7.804	100%

* Valores contemplam movimentação de caixa (não incluem informações contábeis, tais como capitalizações de juros)

O quadro de Usos e Fontes consolida todos os gastos das SPE realizados até o mês de março/15 incluindo o CAPEX e despesas administrativas, detalhando as fontes utilizadas para arcar com esses investimentos.

Observa-se que cerca de 39% dos investimentos foram pagos com recursos advindos de financiamentos tomados diretamente nas SPE (Bridges 1, 2 e 4), 10% foram pagos com recursos oriundos do FI-FGTS e 38% foram pagos com mútuos oriundos dos recursos de acionistas. Os 13% restantes referem-se ao equity classe A e B.

Embora cada SPE tenha índices de alavancagem distintos, como demonstrado no item “Controle de aportes e dívidas SPEs”, a consolidação das SPE já busca a estrutura de capital-alvo de 75% de dívida e 25% de capital próprio. O planejamento individual de cada SPE considera a equalização de todas elas ao nível exigido pelos financiadores de Longo Prazo no momento do primeiro desembolso dos mesmos.

CONTROLE DE APORTES E DÍVIDAS SPE

março-15

Valores em Dólares

EMPRESA	ESTALEIRO	CLASSE B	CLASSE A	CLASSE B	INTERCO - FI FGTS	TOTAL	INTERCOMPANY ²	BRIDGE ³	% Participação		Relação Debt Equity		D/E
									CLASSE A	CLASSE B	Equity	Debt	
ARFADOR	JURONG	PNBV	81.347.617	14.850.538	29.495.217	297.914.619	297.914.619	287.076.932	85%	15%	125.183.372	494.991.153	20%
COPACABANA	EAS	PNBV	67.321.469	11.981.221	26.200.010	172.430.083	172.430.083	146.959.155	85%	15%	106.102.720	311.441.218	25%
GRUINARI	EAS	PNBV	54.393.352	9.625.197	25.515.691	125.600.890	125.600.890	134.511.667	85%	15%	91.138.240	273.912.557	25%
IPANEMA	EAS	PNBV	35.681.459	6.291.804	27.057.966	58.873.258	58.873.258	134.860.170	85%	15%	69.026.249	205.733.428	25%
LEBLON	EAS	PNBV	5.142.165	1.212.165	21.967.095	31.278.432	31.278.432	134.860.170	85%	15%	56.276.101	168.078.602	25%
LEVE	EAS	PNBV	27.247.385	4.803.438	22.068.328	24.785.492	24.785.492	134.860.170	85%	15%	54.120.151	161.645.662	25%
MARAMBAIA	EAS	PNBV	26.894.796	4.741.216	22.450.756	8.537.499	8.537.499	114.165.000	85%	15%	54.086.768	160.702.499	25%
URCA	BRASFELS	ANGRA PART. (OGOG)	73.350.211	12.944.158	38.116.700	174.592.952	174.592.952	211.783.883	85%	15%	124.411.149	488.376.435	20%
GUARAPARI	JURONG	ODF-ELL GALVÃO	57.556.717	14.385.181	42.068.051	250.799.351	250.799.351	182.484.139	80%	20%	114.014.019	433.283.400	21%
BRACUHY	BRASFELS	ANGRA PART. (OGOG)	13.726.626	3.481.158	34.694.149	194.652.381	194.652.381	30.886.066	85%	15%	57.901.933	225.537.246	20%
PORTOGALO	BRASFELS	DOMAIN (PETROBRAS)	5.387.185	1.056.551	15.044.185	54.998.727	54.998.727	30.527.619	85%	15%	22.087.921	85.526.346	21%
MANGARATIBA	BRASFELS	ANGRA PART. (OGOG)	6.055.185	1.068.551	12.377.018	77.103.386	77.103.386	-	85%	15%	19.695.754	77.143.186	20%
BOTINAS	BRASFELS	NEPTUNE (OOG)	6.035.185	1.068.551	12.678.739	17.050.433	17.050.433	-	85%	15%	19.802.475	77.050.433	20%
ONDINA	PARAGUACU	NEPTUNE (OOG)	60.335.255	10.753.268	36.260.142	217.523.169	217.523.169	201.894.935	85%	15%	107.948.665	429.218.104	20%
PITUBA	PARAGUACU	NEPTUNE (OOG)	23.317.661	3.585.458	31.751.018	170.648.803	170.648.803	14.544.867	85%	15%	55.654.137	224.193.670	20%
BOITEBA	PARAGUACU	NEPTUNE (OOG)	13.018.385	2.297.351	20.800.000	101.423.466	101.423.466	44.054.768	85%	15%	36.115.736	145.478.234	20%
INTERLAGOS	PARAGUACU	NEPTUNE (OOG)	6.422.385	1.133.351	22.806.160	23.050.001	23.050.001	37.000.000	85%	15%	30.361.896	60.050.001	34%
ITAPERMA	PARAGUACU	SEAWORTHY (ETESCO/OAS)	8.021.812	2.673.924	23.156.160	1	1	34.000.000	75%	25%	33.851.896	34.000.001	50%
COMANDATUBA	PARAGUACU	SEAWORTHY (ETESCO/OAS)	8.021.812	2.673.924	23.156.160	1	1	34.000.000	75%	25%	33.851.896	34.000.001	50%
FRADE	BRASFELS	DOMAIN (PETROBRAS)	35.790.106	6.260.820	40.285.554	348.548.151	348.548.151	40.699.598	85%	15%	82.336.480	329.242.111	20%
CAMBURI	JURONG	SEABRAS (SEADRILL)	14.324.036	6.224.558	36.023.130	140.795.451	140.795.451	89.027.143	70%	30%	57.371.724	229.120.582	20%
ITAPORA	JURONG	ODF-ELL GALVÃO	9.861.003	2.405.235	27.359.000	19.670.948	19.670.948	70.905.276	80%	20%	39.885.838	100.526.224	20%
ITAUVAIS	JURONG	SEABRAS (SEADRILL)	7.023.635	3.010.101	27.457.747	59.700.000	59.700.000	95.835.000	70%	30%	37.488.483	135.535.000	22%
SIRI	JURONG	ODF-ELL GALVÃO	11.012.282	2.753.054	37.728.000	21.800.001	21.800.001	76.000.000	80%	20%	51.453.336	97.800.001	34%
SAHY	JURONG	SEABRAS (SEADRILL)	8.885.435	3.722.301	38.872.160	20.200.000	20.200.000	71.000.000	70%	30%	51.279.896	91.200.000	36%
CASSINO	ECOVIX	SEAWORTHY (ETESCO/OAS)	45.298.829	14.743.342	31.293.953	204.521.783	204.521.783	157.945.554	75%	25%	91.244.994	365.467.287	20%
CURUMIM	ECOVIX	SEAWORTHY (ETESCO/OAS)	17.824.302	5.941.434	33.611.920	114.622.460	114.622.460	98.519.864	75%	25%	57.378.656	214.142.333	21%
SALINAS	EAS	SEAWORTHY (ETESCO/OAS)	17.320.302	5.773.434	21.443.200	75.471.334	75.471.334	85.662.750	75%	25%	44.536.936	161.133.484	22%
JOATINGA	EAS	ASD	46.045.637	14.056.154	52.900.000	3.037.540.473	3.037.540.473	250.000.000	100%	0%	1.770.701.057	6.182.429.194	22%
TOTAL			821.417.075	184.056.154	784.126.828	3.037.540.473	3.037.540.473	1.134.888.721					

* Valores Contábeis (Incluem a capitalização de juros, quando o caso, nas intercompanhias e Bridges)

1	INTERCO - FI FGTS	Empréstimos subordinados de longo prazo com recursos das Debentures do FI-FGTS. Nas SPE são empréstimos com 15 anos de prazo para amortização, carência total de 9 meses após início da operação, juros de 12% a.a. Para o cálculo de alavancagem, estes recursos são considerados equity.
2	INTERCOMPANY	Empréstimos de curto prazo (ponte) com recursos do Ponte 3, tomado na Sete Internacional, e/ou recursos dos acionistas. Serão repagos quando da entrada de um novo financiamento ponte (ex. Ponte 4) tomado diretamente na SPE ou quando do desembolso da dívida sênior. Nos casos das SPE que possuem empréstimo-ponte contratado, trata-se de um instrumento Subordinado.
3	BRIDGE	Empréstimos de curto prazo tomados diretamente pela SPE (Bridge 1, 2 e 4). Serão repagos quando do 1º desembolso de dívida sênior.

Sete Brasil | Relatório Executivo

09/10

Destaques Gerais

GOVERNANÇA

Conselho de Administração

RCA 15.04.2015

Itens deliberativos:

- Deliberada a revisão de critérios para os benefícios de remuneração de longo prazo dos administradores.

Itens informativos:

- Visão Geral dos Negócios da Companhia;
- Acompanhamento do Plano de Financiamento da Companhia;
- Acompanhamento da evolução da constituição dos ativos;
- Reporte da Auditoria Interna.

Comitê de Auditoria

Reunião
09.04.2015

- Reporte da Auditoria Interna.

Conselho Fiscal

RCF 14.04.2015

- Acompanhamento Orçamentário (orçado x realizado) até fevereiro/2015.

Assembleia Geral

AGO
Reunião 30.04.2015
11h

- Assembleia pendente de fechamento formal de seus acionistas (até a data da divulgação desse Relatório).


AGE
Reunião 30.04.2015
12h

- Assembleia temporariamente em aberto (até a data da divulgação desse Relatório);
- Ordem do dia: deliberar sobre a autorização para que a Companhia possa iniciar os preparativos pré-operacionais das sondas de perfuração do Projeto Sondas.

SOBRE A SETE BRASIL

Criada em dezembro de 2010, a Sete Brasil é uma sociedade anônima de capital fechado especializada em gestão de portfólio de ativos com investimentos voltados para o setor de petróleo e gás na área de *offshore* no Brasil, especialmente aqueles relacionados ao pré-sal brasileiro. A Sete Brasil registra, em sua carteira de projetos, 28 contratos de afretamento e 29 contratos de EPC, onde o portfólio de ativos operacionais é dividido em 23 unidades do tipo navio-sonda e 6 unidades do tipo semissubmersíveis. A Companhia foi criada tendo como acionistas diretos a Petrobras e o fundo de investimento em participações FIP Sondas, formado por investidores institucionais, bancos e fundos de investimento.

Estrutura Societária

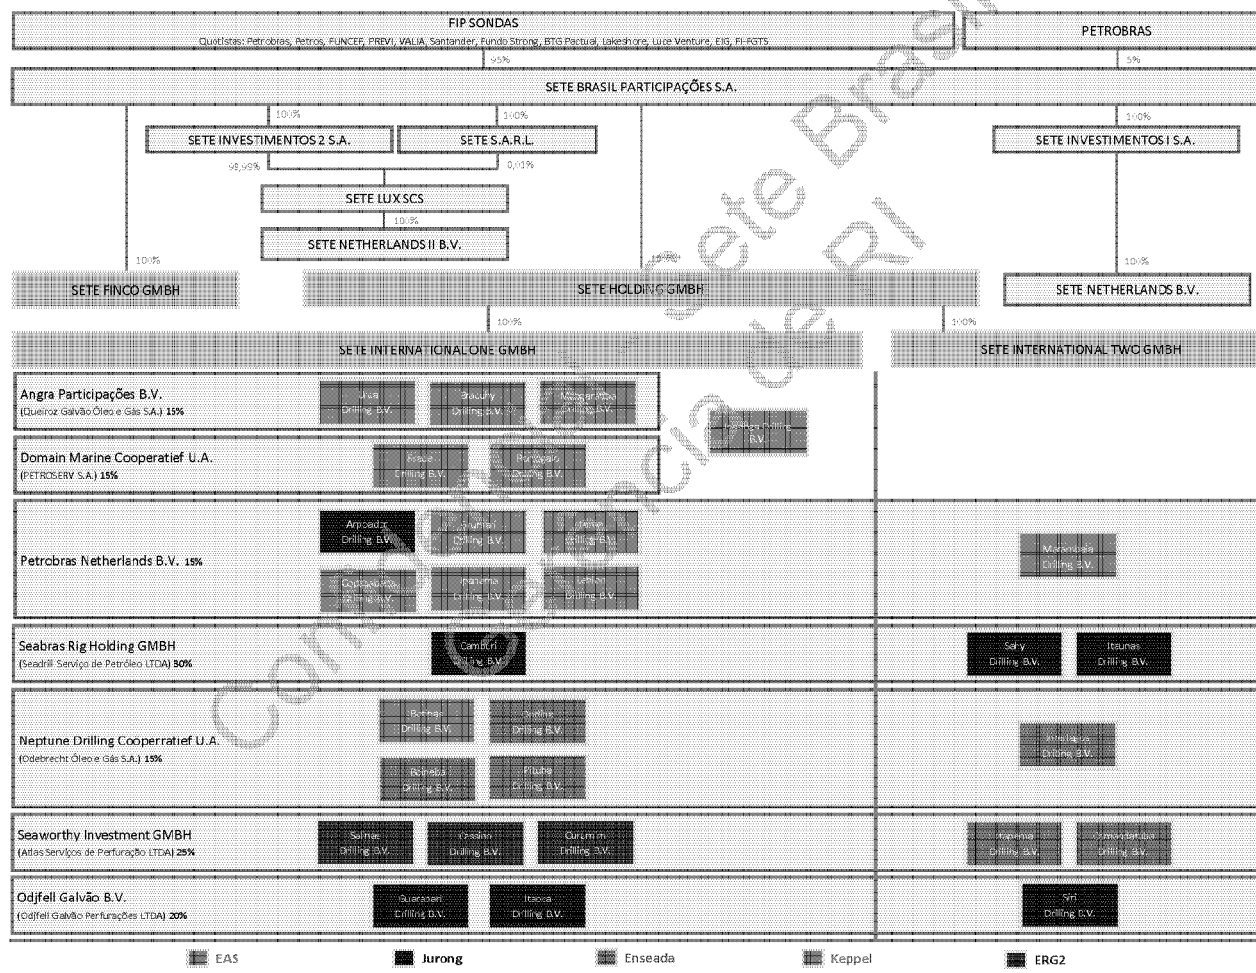

Gerência de Relacionamento com Investidores

ri@setebr.com
www.setebr.com
<http://ri.setebr.com/>
+ 55 21 2528-0080

